Cre8ive Skill

Customer Portal & Self-Service Order Tracking System

How we reduced request processing from days to hours and unlocked growth without headcount

By Sonal Khobragade — Business Analyst | Nov 2024 – Jun 2025

The Brief

In late 2024 I identified an operational constraint at Cre8iveSkill that was limiting growth and eroding client trust: nearly all incoming work arrived via email and was handled manually by the operations team. This meant requests were interpreted by different people in different ways, data was duplicated across spreadsheets, and customers got inconsistent responses and very little visibility. I led the end-to-end design and delivery of a Customer Portal & Self-Service Order Tracking System that centralized intake, enforced structured data capture, automated routing and provided customers with real-time status and downloadable proofs.

My work began with quantitative diagnosis — timed process walkthroughs to set baselines — and extended to stakeholder alignment with top clients and internal users to validate needs. I authored the business case showing clear ROI, translated requirements into prioritized user stories, and designed a lightweight, integrable architecture combining portal, email ingestion and API hooks.

The result was a move from reactive, people-dependent processes to a predictable, auditable workflow that freed the team to focus on higher-value work and delivered a professional customer experience that supported scaled growth.

Project Scope

- End-to-end business analysis and requirements engineering
- Customer portal design with self-service order tracking
- Automated email ingestion and routing system
- API integration with production scheduling
- Change management and user adoption program

8
Months Duration

3
Major Client Stakeholders

100%
At-Risk Client Retention

The Challenge

The challenge was both operational and strategic. Operationally, the ops team spent roughly 160 hours per month on email triage and duplicate data entry — about 40% of their productive time — creating fatigue, errors and slow throughput. Strategically, three major clients were unhappy with slow turnaround and lack of visibility, which put material revenue at risk. There was no single source of truth: requests were spread across inboxes, ad hoc spreadsheets and informal notes, so managers could not measure throughput or confidently forecast capacity.

I quantified the impact: a persistent 18–22% follow-up/error rate caused rework, and average assignment latency of 3–5 days blocked responsiveness. The business could not scale because each incremental order demanded proportionate manual effort.

My brief was clear but demanding: design a customer-facing, operationally rigorous system that improved data quality at capture, shortened assignment times, slashed follow-ups, and enabled measurable capacity growth — all while being easy for customers and internal teams to adopt and demonstrating fast, trackable ROI to secure leadership support.

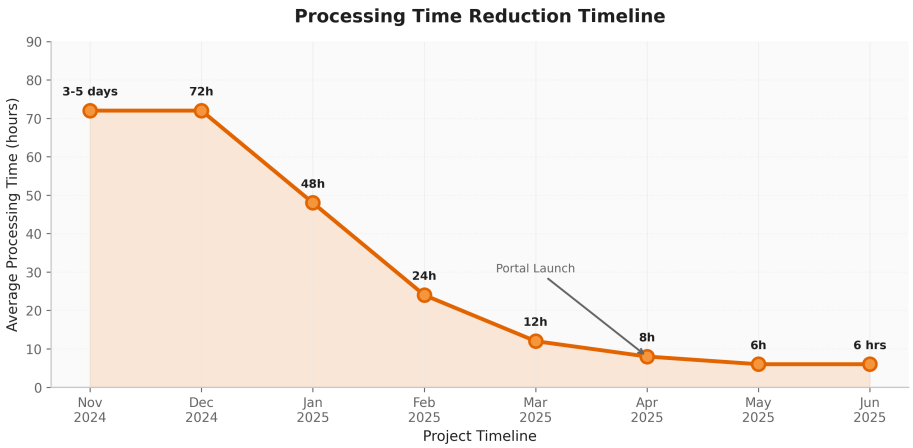

Figure 1: Processing time reduction from 3-5 days to 6 hours over the project timeline

Challenge Area	Before State	Impact
Email Triage	160 hrs/month manual processing	40% of productive time lost
Assignment Time	3-5 days average	Blocked responsiveness
Error Rate	18-22% follow-up rate	Significant rework required
Data Visibility	No single source of truth	Unable to forecast capacity

Our Approach

Process, Analysis & Design

My approach combined forensic process analysis with market and gap assessments to ensure the solution solved immediate pain and aligned with market expectations. I started with gap analysis to compare the current state against a target operating model: timed walkthroughs, BPMN maps and a capability grid revealed specific process, data and governance shortfalls.

I performed a market analysis and informal competitor scan to learn how peer providers offered portal features and SLAs, and used those insights to shape feature prioritization. I also ran a concise SWOT analysis with stakeholders to identify internal strengths we could leverage, such as skilled digitizers, and weaknesses to mitigate, such as ad-hoc email habits; opportunities included retention of at-risk clients and operational leverage, while threats included potential churn.

Based on this evidence I developed a quantified business case and prioritized backlog. Requirements were gathered through role-based workshops; I co-designed guided submission forms and wireframes with users, translated needs into user stories with strict acceptance criteria, and maintained a traceability matrix so every requirement mapped to a test and UI element. Architecture specified portal + email ingestion + API hooks and prioritized assignment queues integrated with production scheduling — deliberately choosing observability and auditability as design principles.

Analysis Methods

- Gap Analysis
- Market Analysis
- SWOT Analysis
- BPMN Process Mapping
- Competitor Benchmarking

Design Outputs

- Quantified Business Case
- Prioritized User Stories
- Wireframes & Mockups
- Requirements Traceability Matrix
- System Architecture

Our Approach

Implementation, UAT & Change Management

During implementation I operated as the single point of clarity between business users and the outsourced development team. I clarified user stories in JIRA, reviewed weekly design proposals, and validated that database models and UI flows supported both operational queries and reporting needs.

For quality assurance I created realistic UAT scenarios that represented edge and high-complexity cases — rush digitizing with embroidery constraints, multi-file proofs and staged approvals — and recruited representative users to execute tests. I led daily triage during UAT to prioritize fixes against impact and adoption risk; I enforced acceptance criteria that covered functional, performance and UX thresholds.

Simultaneously I led change management: role-based training, quick reference cards, short video walkthroughs, and an internal communications plan that explained the "why" and the benefits. I also organized a 72-hour hypercare support window post-launch and staffed a support rota to capture early issues and reinforce new behaviors. Within the first week I hosted a retrospective using live performance data to prioritize early fixes, and the iterative fixes plus strong support prevented fallback to old email habits and ensured the new process stuck.



Change Management Program

- Role-based training sessions for all user types
- Quick reference cards for common workflows
- Video walkthroughs for self-paced learning
- Internal communications explaining benefits and "why"
- 72-hour hypercare support window post-launch
- Weekly retrospective with live performance data

The Value & Outcome I Delivered

The results were measurable and strategically meaningful. After launch manual email handling fell by 73%, and average assignment time collapsed from 3–5 days to about 6 hours — an operational acceleration that enabled faster customer response and better scheduling. Follow-up/error rates dropped from 18–22% to 1.2%, returning data quality and reducing rework. The operations team reclaimed roughly 870 annual labor hours, representing approximately $32,400 in labor savings, and the platform unlocked about 40% additional capacity without hiring headcount.

Critically, the three at-risk clients remained and expanded their orders by around 35% on average, preserving and growing revenue. Beyond the headline metrics, we delivered cleaner, auditable data for forecasting and negotiations, improved client confidence via real-time tracking, and a repeatable framework (gap analysis → requirements → UAT → change management) for future operational automations.

In short, the project converted a fragile, error-prone process into a scalable capability that improved customer experience and positioned Cre8iveSkill for sustained growth.



Figure 2: Key performance metrics comparing before and after implementation

73%
Email Handling Reduction

94%
Error Rate Reduction

$32.4K
Annual Labor Savings

35%
Client Order Expansion
